FORM R.L.-7 REV. 2-40

SHEET 1 OF 1

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 3513
TRUNK HIGHWAY 220
COUNTY Kittson
DISTRICT 2B

LIMITS: S. Co. Line – Jct. T.H. 11

Ref. Pt. 075+00.157 - 077+00.162

YEAR BUILT	PROJECT Nº	DESCRIPTION TYPE	WIDTH	THICKNESS	REMARKS	CODE Nº DIST
		Gravel	28'		No Record of Const. Added in 1949	
M 1956	A.F.E. 606	Grav. Resurfacing			784 Tons	
C 1960	3513-02	Grading	38'			
		Gravel	30'		1895 Tons Gravel	1059
M 1961		Gravel Resurfacing			1008 Tons	
C 1962	3513-04	Soil Cement Base	23'	7"		
		Plant Mix Bit. (Base)	22'	1½"		362
M 1967	C	Light Bit. Seal	23'		CRS-1, 4050 Gal. Agg. 120 C.Y.	367
C 1971	3513-06	Plant Mix Bit. Surf.	22'	1½"		870
C 1993	3513-09	Bit. Overlay	26'	2"	Spec. 2331	
M 1998	M98295	Aggregate Seal				
S 2011	3513-11	Milling	26'	3"	Spec 2360	
		Bit. Overlay	26'	3"		

PLAN



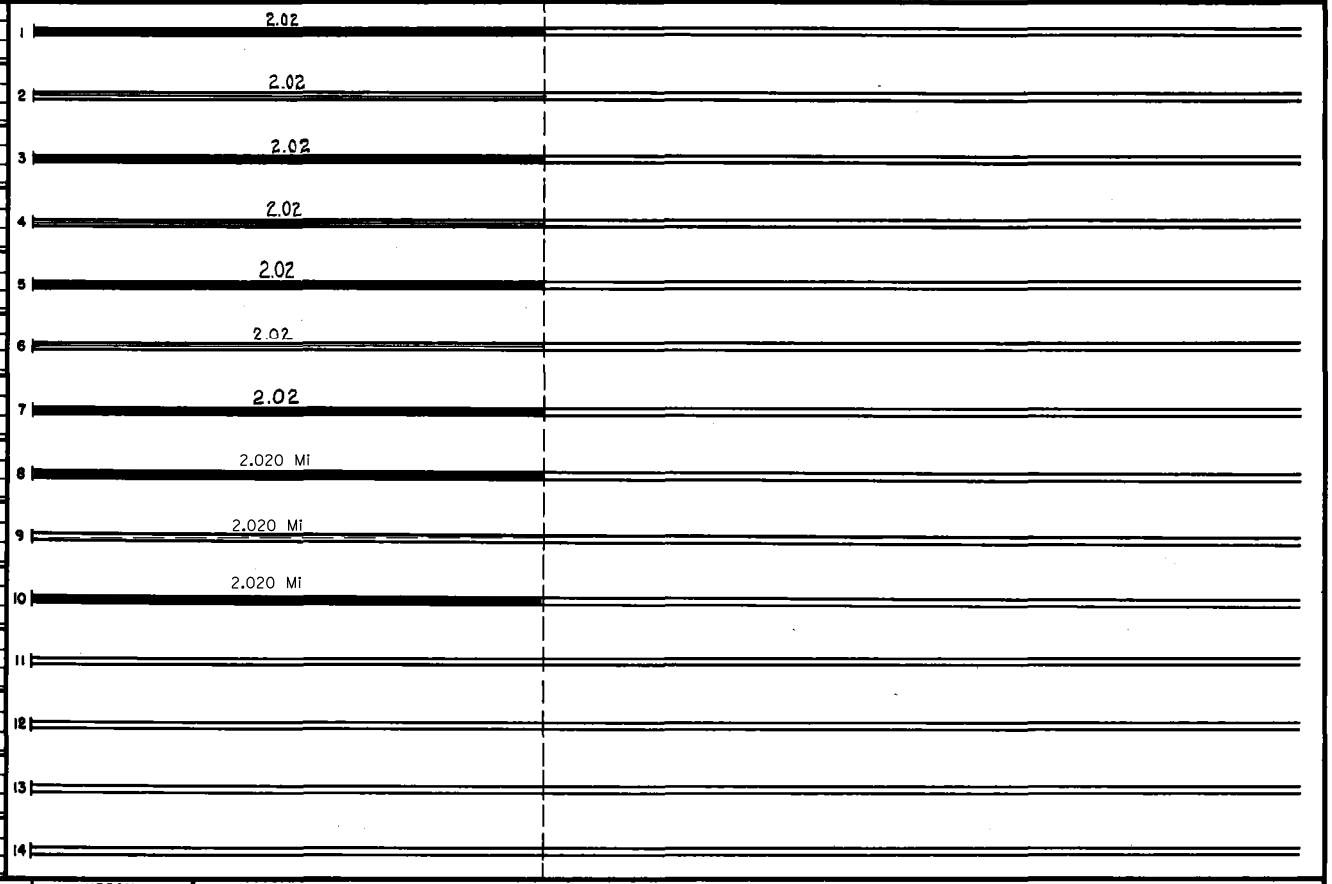

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1949		2.02	2.02	0.00	0.00	0.00	2.02	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1949
